

# US Hwy 14 (6<sup>th</sup> Street) Reconstruction

20<sup>th</sup> Ave to 34<sup>th</sup> Ave

**Newsletter #18**

**November 9<sup>th</sup>, 2017**



**PROJECT INFO**

Contract Amount  
**\$16,353,880.86**

Completion Date  
**June 30, 2018**

**Project Website link**  
<http://www.sddot.com/travelers/projects/6thStBrkgs/default.aspx>

Contract No:  
 PH 0014(177)421 PCN 546N  
 IM 0295(40)132 PCN 04TW  
 WW 1601 PCN X03N


The project will be completed in 3 Major Phases.

- Phase 1A – north side of 6<sup>th</sup> Street
- Phase 1B – 22<sup>nd</sup> Ave intersection
- Phase 2 – south side of 6<sup>th</sup> Street
- Phase 3 – medians / service roads

The current status of these phases is shown in the graphic below.

**Project Update**

- **Hwy 14 work summary**
  - Median work continues.
  - Sealing of the roadway concrete joints continues.
  - A drainage channel will be cleaned-out along the south side, from 32<sup>nd</sup> Ave to the east.
  - Final grading of the topsoil at the sidewalks and curb ramps will be occurring.
  - Final pavement markings will be installed at all locations.
  - Lane closures will be installed as this work continues.
- **Bridge work summary**
  - Pedestrian rail is being installed on the Hwy 14 bridge @ I-29.
- **I-29 work summary**
  - Guardrail is being installed along the southbound lanes of I-29.
  - The crossovers will be removed, between Hwy 14 and the Bypass.
  - The head-to-head traffic conditions of I-29 will be removed, with lane closures being installed to finish the northbound lanes guardrail work.

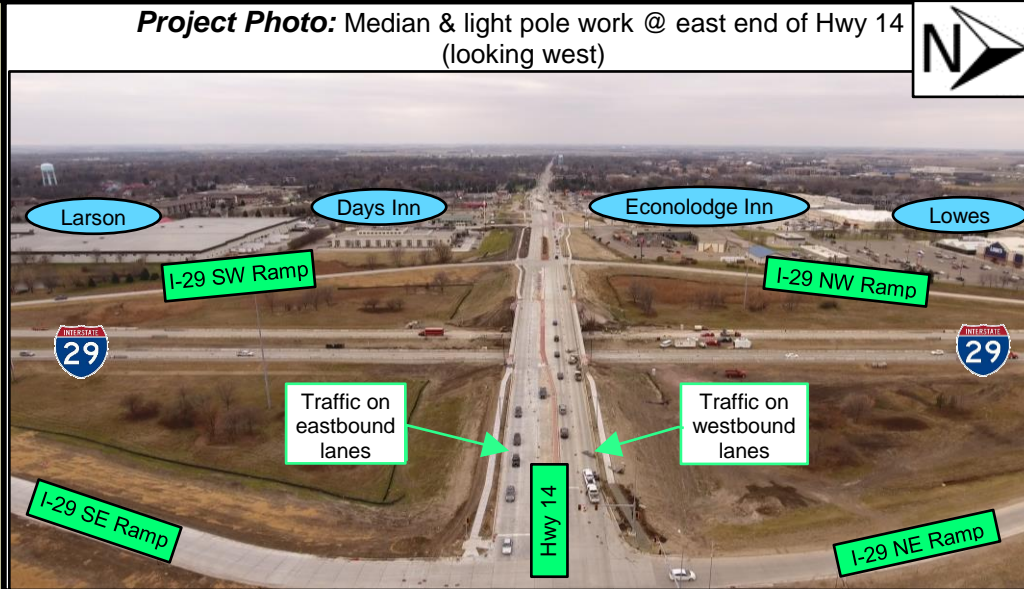

- This will be the **last newsletter** for the 2017 season.
  - Work will soon stop due to cold weather & snow conditions.
  - The service roads west of I-29 will remain in-place thru this winter.
- Work will resume Spring 2018.
  - The service roads west of I-29 will be altered / removed in Spring 2018.
  - This service road work and all final items will be completed by June 30, 2018.
- Thank You **very much** for your patience during all of this work!!!
  - This was a very challenging project, but we made it through.
  - Please give **BX Civil & Construction** a special **THANKS** for all of their hard work!!!

**PROJECT TEAM**

**South Dakota DOT**  
 Connecting South Dakota and the Nation

John Rittershaus, Project Manager  
[john.rittershaus@state.sd.us](mailto:john.rittershaus@state.sd.us)  
 Office: (605) 688-5003  
 Cell: (605) 881-7145

**BX Civil & Construction**

Nic Auringer, Project Manager  
[nauringer@bx-cc.com](mailto:nauringer@bx-cc.com)  
 Office: (605) 428-5483  
 Cell: (605) 351-4350

**brookings**  
 SOUTH DAKOTA

City of Brookings  
 Jackie Lanning, City Engineer  
[jlanning@cityofbrookings.org](mailto:jlanning@cityofbrookings.org)  
 Office: (605) 692-6629  
 Cell: (605) 691-3567

**BROOKINGS**  
 municipal utilities

Brookings Municipal Utilities (BMU)  
 Eric Witt, Project Engineer  
[ewitt@swiftel-bmu.com](mailto:ewitt@swiftel-bmu.com)  
 Office: (605) 697-8410  
 Cell: (605) 691-3334

**HR**

To receive your newsletter by email, send a request to  
[lance.mcqueen@hdrinc.com](mailto:lance.mcqueen@hdrinc.com)
